FUTURE FOCUSED PLANNING · SITE DEPLOYMENT

SITE DEPLOYMENT PLAYBOOK

From Day 0 to Hypercare Exit

How I would deploy a new planning Target Operating Model at a manufacturing site. Checklists, scorecards and templates included.

Built on The L.I.L.Y Method

Lean Integration Lets You · Discovery by Execution

FELIPE BART Supply Planning Transformation

SWIPE ▶

THE LIFECYCLE ON ONE PAGE

Six phases. Six gates. No site left behind.

1

ASSESS

Readiness scorecard, stakeholder map, baseline KPIs.

Wk 0-3

Gate: Readiness signed off

2

PLAN

Site deployment plan, change plan, training design.

Wk 3-5

Gate: Plan approved by site head

3

TRAIN

Role-based learning and a live TOM emulation.

Wk 5-10

Gate: Competence verified

4

GO-LIVE

Cutover to the new TOM with daily huddles.

Wk 10-12

Gate: Go / no-go checklist

5

HYPERCARE

Floor-walking support, issue burn-down, coaching.

Wk 12-20

Gate: Exit criteria met

6

SUSTAIN

Site owns it: audits, refreshers, shared learnings.

Wk 20+

Gate: Handover to site owner

DISCOVERY BY EXECUTION runs through every phase

Emulate the TOM with today's tools, run it for real, and let the bottlenecks show themselves before go-live. Typical durations; adapt to each site.

MY DIFFERENTIATOR

Discovery by Execution: test the TOM before the tools arrive

L.I.L.Y

Lean Integration Lets You

Emulate the Target Operating Model with the tools a site already has, so culture change starts before the new tools land.

THE DISCOVERY BY EXECUTION LOOP

1 EMULATE

Mirror TOM roles, cadence and decisions using today's tools: Excel, SAP, current meetings.

2 EXECUTE

Run real planning cycles the new way. Practice, not a slide about intent.

3 DISCOVER

Bottlenecks, hand-offs and resistance surface as data, not opinion.

4 ADJUST

Fix the design or the habit, then scale into the full tool rollout.

Culture change starts early

Bottlenecks found before go-live

Better odds of project success

PHASE 1 · ASSESS

Site readiness scorecard

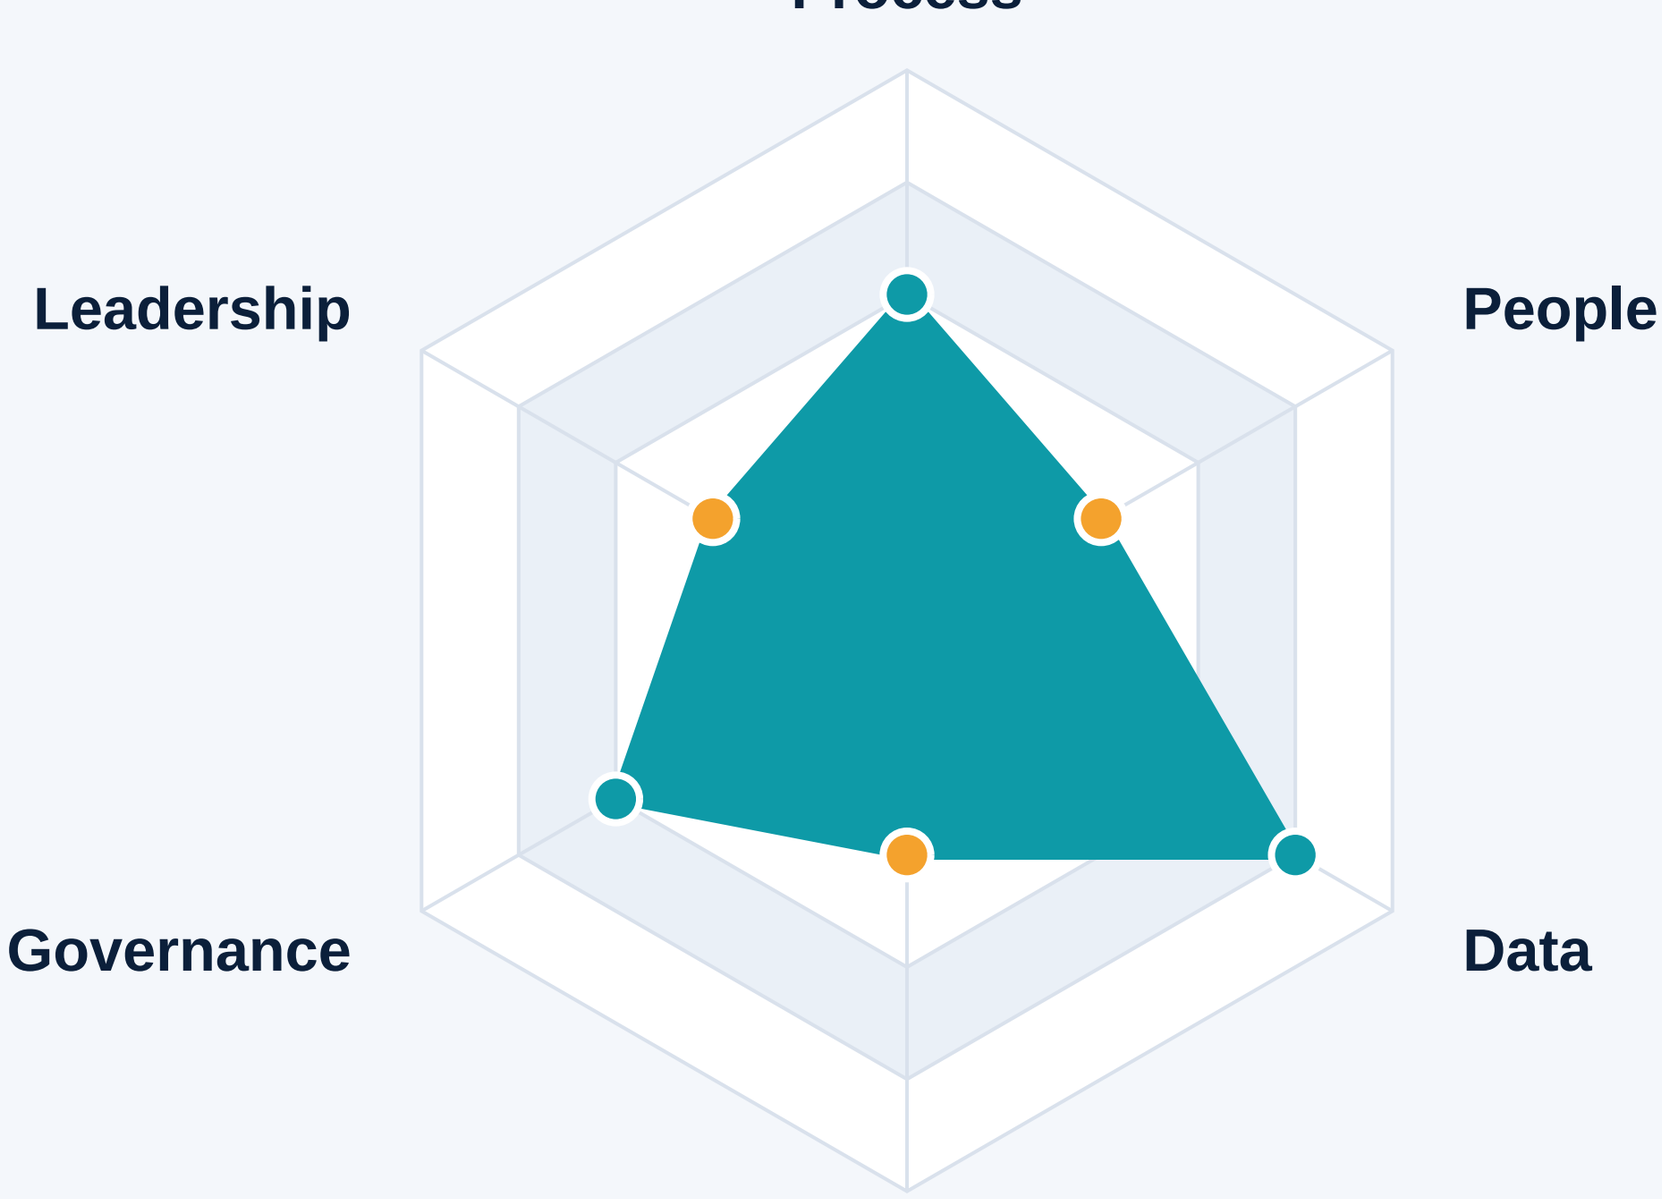

1 Ad hoc	2 Emerging	3 Defined	4 Managed	5 Embedded

Illustrative scores. Any dimension at 2 or below (amber) becomes a named gap in the deployment plan, with an owner and a date.

PHASE 1 · ASSESS

Stakeholder map: who matters at site

1	**Site Head**	Weekly 1:1. Frame wins as service, cost and compliance.
2	**Supply Chain Lead**	Co-own site adaptations and KPI targets.
3	**Operations**	Involve in S&OP inputs. Fix the hand-offs they feel.
4	**Planners**	Coach daily. Recruit 2 to 3 peer champions early.
5	**Global Deployment Lead**	One page, every week: progress, risks, asks.

PHASE 2 · PLAN

Site deployment plan template

EVERY WORKSTREAM CARRIES FOUR FIELDS

OWNER
One named person

MILESTONE
Dated and measurable

RISK
What could slip

DEPENDENCY
What it waits on

EXAMPLE ROW

Training delivery

Owner: Site planning lead

Milestone: 100% of planners certified, week 10

Risk: Shift patterns clash with sessions

Depends on: TOM sandbox ready by week 6

PHASE 2 · PLAN

Change management: meet resistance with a plan

A	D	K	A	R
Awareness	Desire	Knowledge	Ability	Reinforce

WHAT PLANNERS SAY, AND WHAT I DO ABOUT IT

"My spreadsheet is more accurate."

RESPONSE

Run both side by side for two cycles. Let the data decide, then retire the old way.

"I don't have time to learn this."

RESPONSE

Build learning into the weekly cycle: 30 minutes of practice on real orders.

"Corporate doesn't understand our site."

RESPONSE

Co-design site adaptations inside TOM guardrails. Planners own them.

"It will all go back after hypercare."

RESPONSE

Reinforce: named owners, audits, and TOM KPIs inside the site review.

PHASE 3 · TRAIN

Training that proves capability, not attendance

AUDIENCE	FORMAT	FOCUS
Planners	Hands-on labs on real data	Run the full cycle in the TOM
Site leadership	60-min briefing and decision walk-through	Read the dashboard, ask the right questions
Ops and production	Scenario workshop	Inputs, hand-offs and lead times
Site champions	Train-the-trainer	Coach peers, own the refreshers

Verify competence, not attendance

Every learner climbs the ladder. Nobody is marked trained until they reach step 3.

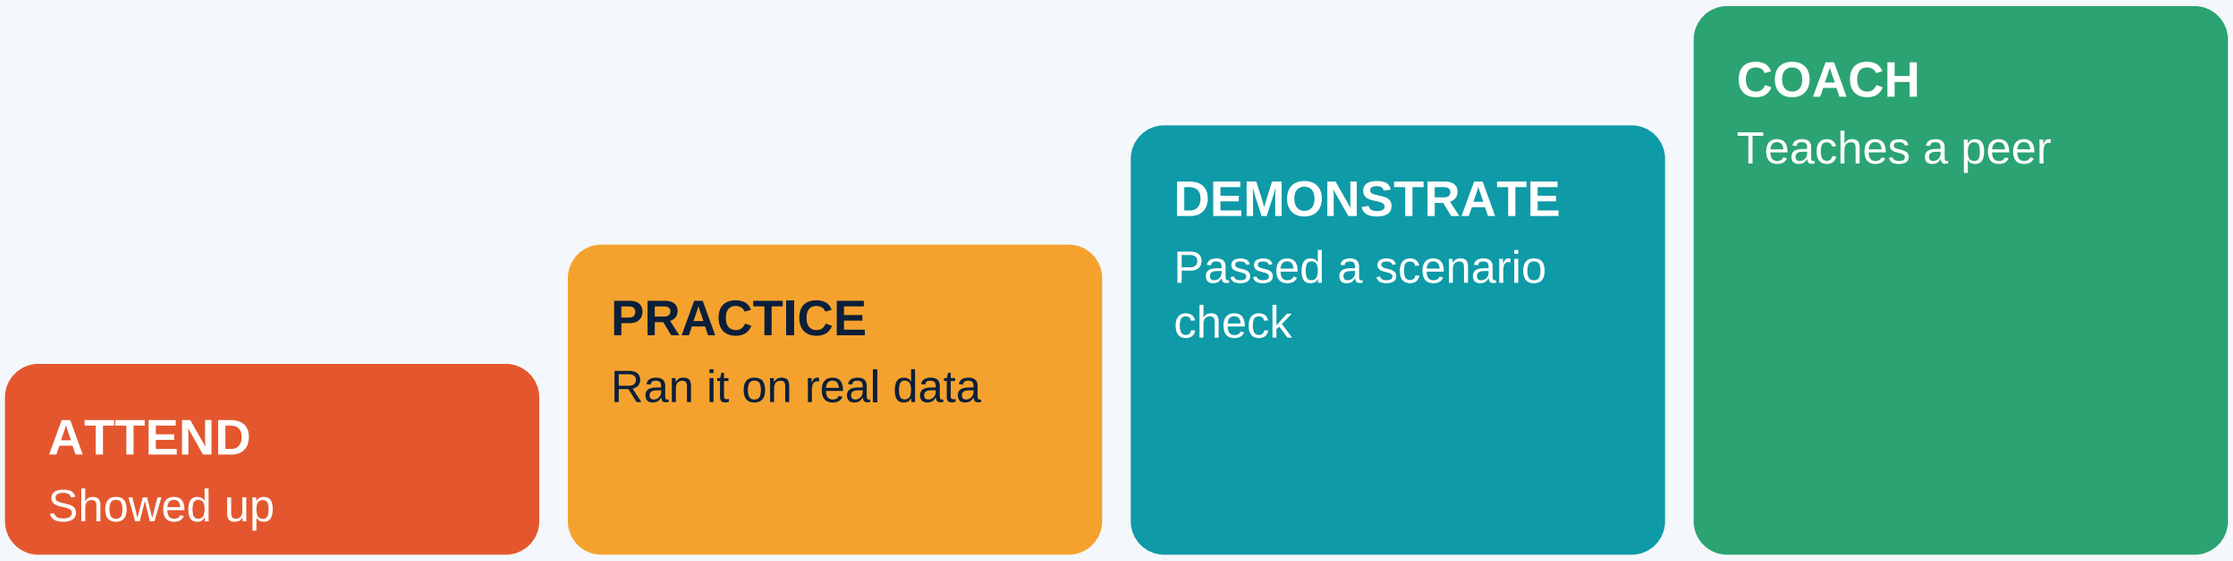

PHASE 4 · GO-LIVE

The weekly cadence that keeps it moving

DAILY
15 min

Site huddle

Agenda: yesterday's cycle, blockers, today's focus.

Output: blocker log updated, owners assigned.

WEEKLY
60 min

Site working session

Agenda: run the TOM cycle live, review exceptions and bottlenecks.

Output: fix list and training gaps flagged.

WEEKLY
30 min

Steering with site leadership

Agenda: progress against milestones, decisions needed.

Output: decisions logged, risks escalated.

WEEKLY
1 page

Report to Deployment Lead

Agenda: RAG status, KPIs, risks, asks, learnings.

Output: aligned support and cross-site insight.

PHASE 4 · GO-LIVE

KPI dashboard: lead with leading indicators

LEADING: move first

Training completion
Weekly

82% sample

Process compliance
Weekly

74% sample

Planner confidence
Pulse survey

68% sample

Issue closure rate
Weekly

60% sample

LAGGING: prove results

Forecast accuracy
Monthly

78% sample

Plan adherence
Monthly

70% sample

Inventory days
Monthly

55% sample

Service level (OTIF)
Monthly

90% sample

Leading indicators tell you what will happen. Lagging ones prove it did. Report both, every week.

Sample values shown for illustration.

PHASE 4 · GO-LIVE

Risk and escalation ladder

L1
LEVEL

Me, at site

Handles: process gaps, training tweaks, local adoption issues.

Go up if: no fix in 5 working days, or a milestone is at risk.

L2
LEVEL

Site Head

Handles: resourcing, priority conflicts, planner availability.

Go up if: it needs a cross-site or tool change, or 2 weeks of slip.

L3
LEVEL

Deployment Lead

Handles: tool defects, TOM design questions, cross-site dependencies.

Go up if: scope, budget or timeline is affected.

L4
LEVEL

Program steering

Decides: scope, budget, timeline and strategic trade-offs.

Arrives with a clear recommendation and options.

Escalate early, with a recommendation. Never just a problem.

PHASE 5 · HYPERCARE

Hypercare exit checklist

PERFORMANCE

- [ ] KPIs at target for 4 consecutive weeks.
- [ ] Zero critical issues open; high-priority issues inside the agreed threshold.

PEOPLE

- [ ] 100% of planners passed the competence check.
- [ ] Site champions coach new joiners without me.

PROCESS

- [ ] TOM cycles run end to end for 4 cycles with no central support.
- [ ] Process compliance above the agreed threshold.

GOVERNANCE

- [ ] Named site owner; TOM KPIs sit in the site review.
- [ ] Audit calendar set; lessons logged and shared with the program.

PHASE 6 · SUSTAIN

Close the loop. Pass it on.

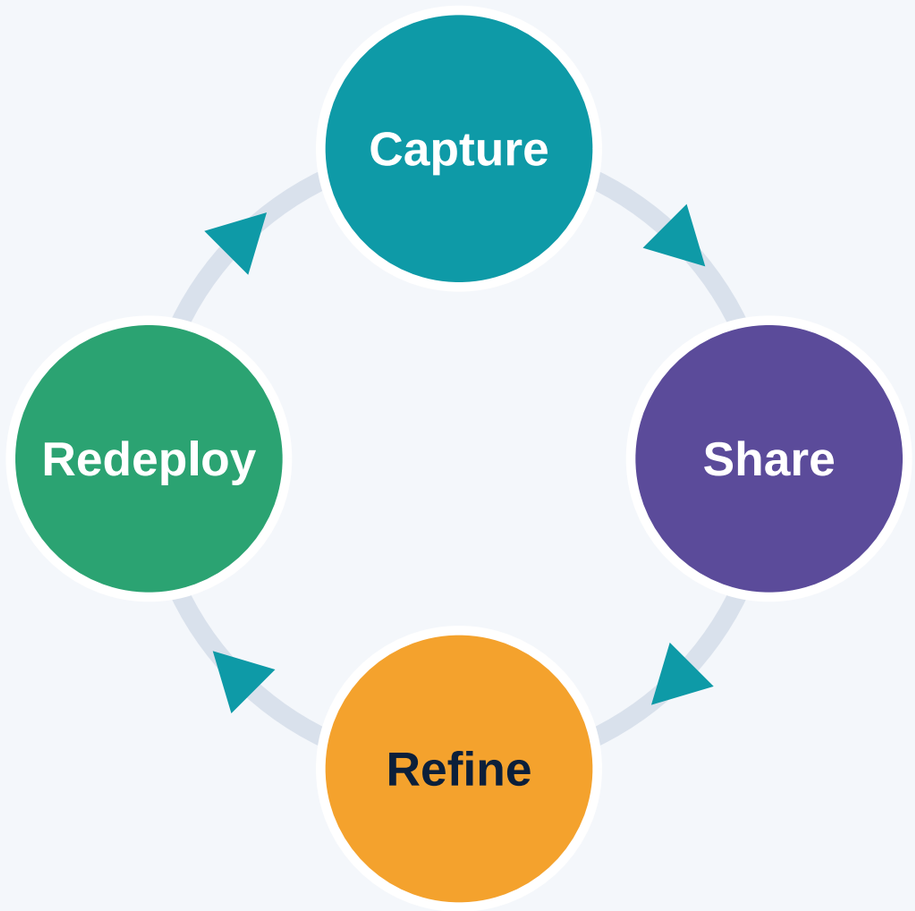

Every site teaches the next

Capture: what worked, broke and surprised.

Share: with the central program, weekly.

Refine: the deployment approach.

Redeploy: the improved playbook at the next site.

CURATED LEARNING

ASCM (APICS) supply chain resources	ascm.org
Prosci ADKAR change model	prosci.com
SAP Learning for planning tools	learning.sap.com
Lean Enterprise Institute	lean.org

Want the editable templates?

Comment PLAYBOOK or message me.

Felipe Bart · Supply Planning Transformation
